
ID	Task Mode	Task Name	Locale	Duration	Start	Finish	RP Start	RP End	Length	Width	Area	Treatmer	Est App Rate	Est Litres	Predecessors
1		**Mackenzie DC Resurfacing**		**18.5 days**	**Mon 23/11/26**	**Thu 17/12/26**									
2		ERUBUS PLACE	Tekapo	0.3 days	Mon 30/11/26	Mon 30/11/26	9	84	75	9	675	TC46	2.35	1586.25	
3		D'ARCHIAC DRIVE	Tekapo	0.3 days	Mon 30/11/26	Mon 30/11/26	578	669	91	10.4	946.4	TC46	2.35	2224.04	2
4		D'ARCHIAC DRIVE	Tekapo	0.3 days	Mon 30/11/26	Mon 30/11/26	457	578	121	10.4	1258.4	TC46	2.35	2957.24	3
5		CAIRNS AVENUE	Tekapo	0.5 days	Mon 30/11/26	Tue 1/12/26	31	182	151	12.9	1947.9	TC46	2.35	4577.565	4
6		COULSON LANE	Tekapo	0.1 days	Tue 1/12/26	Tue 1/12/26	0	11	11	8.5	93.5	TC46	2.35	219.725	5
7		COULSON LANE	Tekapo	0.2 days	Tue 1/12/26	Tue 1/12/26	17	154	137	8.5	1164.5	TC46	2.35	2736.575	6
8		JIMMYS LANE	Tekapo	0.2 days	Tue 1/12/26	Tue 1/12/26	3	113	110	8.2	902	TC46	2.35	2119.7	7
9		EDWARDS LANE	Tekapo	0.3 days	Tue 1/12/26	Wed 2/12/26	3	212	209	8.2	1713.8	TC46	2.35	4027.43	8
10		ANDREW DON DRIVE	Tekapo	0.5 days	Wed 2/12/26	Wed 2/12/26	291	600	309	10.4	3213.6	TC46	2.35	7551.96	9
11		RODMAN LANE	Tekapo	0.2 days	Wed 2/12/26	Wed 2/12/26	15	142	127	8.4	1066.8	TC46	2.35	2506.98	10
12		ALLAN STREET	Tekapo	0.5 days	Wed 2/12/26	Thu 3/12/26	0	156	156	10.6	1653.6	TC46	2.35	3885.96	11
13		GREIG STREET	Tekapo	0.1 days	Thu 3/12/26	Thu 3/12/26	0	85	85	9.3	790.5	TC46	2.35	1857.675	12
14		LILYBANK ROAD	Tekapo	0.3 days	Thu 3/12/26	Thu 3/12/26	2300	2635	335	6.4	2144	TC35	2.4	5145.6	13
15		LILYBANK ROAD	Tekapo	1 day	Thu 3/12/26	Fri 4/12/26	0	2050	2050	6.3	12915	TC35	2.4	30996	14
16		LILYBANK ROAD	Tekapo	0.2 days	Fri 4/12/26	Fri 4/12/26	2050	2300	250	6.5	1625	TC35	2.4	3900	15
17		CLAYTON ROAD	Fairlie	0.5 days	Mon 7/12/26	Mon 7/12/26	2221	3435	1214	7	8498	TC35	2.4	20395.2	16
18		CLAYTON ROAD	Fairlie	0.3 days	Mon 7/12/26	Mon 7/12/26	15109	15488	379	6.4	2425.6	TC35	2.4	5821.44	17
19		CLAYTON ROAD	Fairlie	0.5 days	Mon 7/12/26	Tue 8/12/26	13825	14913	1088	6	6528	TC35	2.4	15667.2	18
20		CLAYTON ROAD	Fairlie	0.2 days	Tue 8/12/26	Tue 8/12/26	14913	14963	50	3.8	190	TC35	2.4	456	19
21		CLAYTON ROAD	Fairlie	2 days	Tue 8/12/26	Thu 10/12/26	4554	9318	4764	7.29	34729.56	TC35	2.4	83350.944	20
22		CLAYTON ROAD	Fairlie	0.2 days	Thu 10/12/26	Thu 10/12/26	14963	15091	128	6.4	819.2	TC35	2.4	1966.08	21
23		CLAYTON ROAD	Fairlie	0.1 days	Thu 10/12/26	Thu 10/12/26	15091	15109	18	3.4	61.2	TC35	2.4	146.88	22
24		KERR RD	Fairlie	0.1 days	Thu 10/12/26	Thu 10/12/26	1304	1340	36	3.4	122.4	TC35	2.4	293.76	23
25		HAMILTON ROAD	Fairlie	0.3 days	Thu 10/12/26	Fri 11/12/26	7061	7500	439	6	2634	TC35	2.4	6321.6	24
26		HAMILTON ROAD	Fairlie	0.5 days	Fri 11/12/26	Fri 11/12/26	5969	7061	1092	6	6552	TC35	2.4	15724.8	25
27		HAMILTON ROAD	Fairlie	0.1 days	Fri 11/12/26	Fri 11/12/26	3964	4305	341	6	2046	TC35	2.4	4910.4	26
28		HAMILTON ROAD	Fairlie	0.5 days	Fri 11/12/26	Mon 14/12/26	4305	5439	1134	6	6804	TC35	2.4	16329.6	27
29		HAMILTON ROAD	Fairlie	0.2 days	Mon 14/12/26	Mon 14/12/26	5439	5657	218	6	1308	TC35	2.4	3139.2	28
30		HAMILTON ROAD	Fairlie	0.2 days	Mon 14/12/26	Mon 14/12/26	5657	5849	192	6	1152	TC35	2.4	2764.8	29
31		HAMILTON ROAD	Fairlie	0.1 days	Mon 14/12/26	Mon 14/12/26	5849	5969	120	6	720	TC35	2.4	1728	30
32		MOUNT MICHAEL ROAD	Fairlie	0.5 days	Mon 14/12/26	Tue 15/12/26	475	1380	905	5.5	4977.5	TC35	2.4	11946	31
33		TALBOT ROAD	Fairlie	0.3 days	Tue 15/12/26	Tue 15/12/26	618	1172	554	5.7	3157.8	TC35	2.4	7578.72	32
34		TALBOT ROAD	Fairlie	0.3 days	Tue 15/12/26	Tue 15/12/26	175	531	356	5.7	2029.2	TC35	2.4	4870.08	33
35		TALBOT ROAD	Fairlie	0.2 days	Tue 15/12/26	Wed 16/12/26	531	618	87	5.7	495.9	TC35	2.4	1190.16	34
36		O'NEILL ROAD	Albury	0.2 days	Wed 16/12/26	Wed 16/12/26	25	345	320	4.5	1440	TC35	2.4	3456	35
37		GUDEX ROAD	Raincliff	1.2 days	Wed 16/12/26	Thu 17/12/26	4905	8028	3123	6.2	19362.6	TC35	2.4	46470.24	36
38		MIDDLE ROAD	Raincliff	0.1 days	Thu 17/12/26	Thu 17/12/26	0	105	105	5.5	577.5	TC35	2.4	1386	37
39		SPUR ROAD	Raincliff	0.2 days	Thu 17/12/26	Thu 17/12/26	1376	2094	718	5.6	4020.8	TC35	2.4	9649.92	38
40		CANNINGTON ROAD	Pareora	0.2 days	Thu 17/12/26	Thu 17/12/26	5307	5491	184	6	1104	TC35	2.4	2649.6	39



Project: Mackenzie DC 26-27 R
Date: Fri 20/11/26


Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		

ID	Task Mode	Task Name	Locale	Duration	Start	Finish	RP Start	RP End	Length	Width	Area	Treatmer	Est App Rate	Est Litres	Predecessors
41		PAREORA GORGE ROAD JUNCTION	Pareora	0.1 days	Fri 18/12/26	Fri 18/12/26	0	79	79	4.4	347.6	TC35	2.4	834.24	40
42			Rain allowa	3 days	Mon 14/12/26	Thu 17/12/26									

W T F S S 9


Project: Mackenzie DC 26-27 R
Date: Fri 20/11/26

Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		

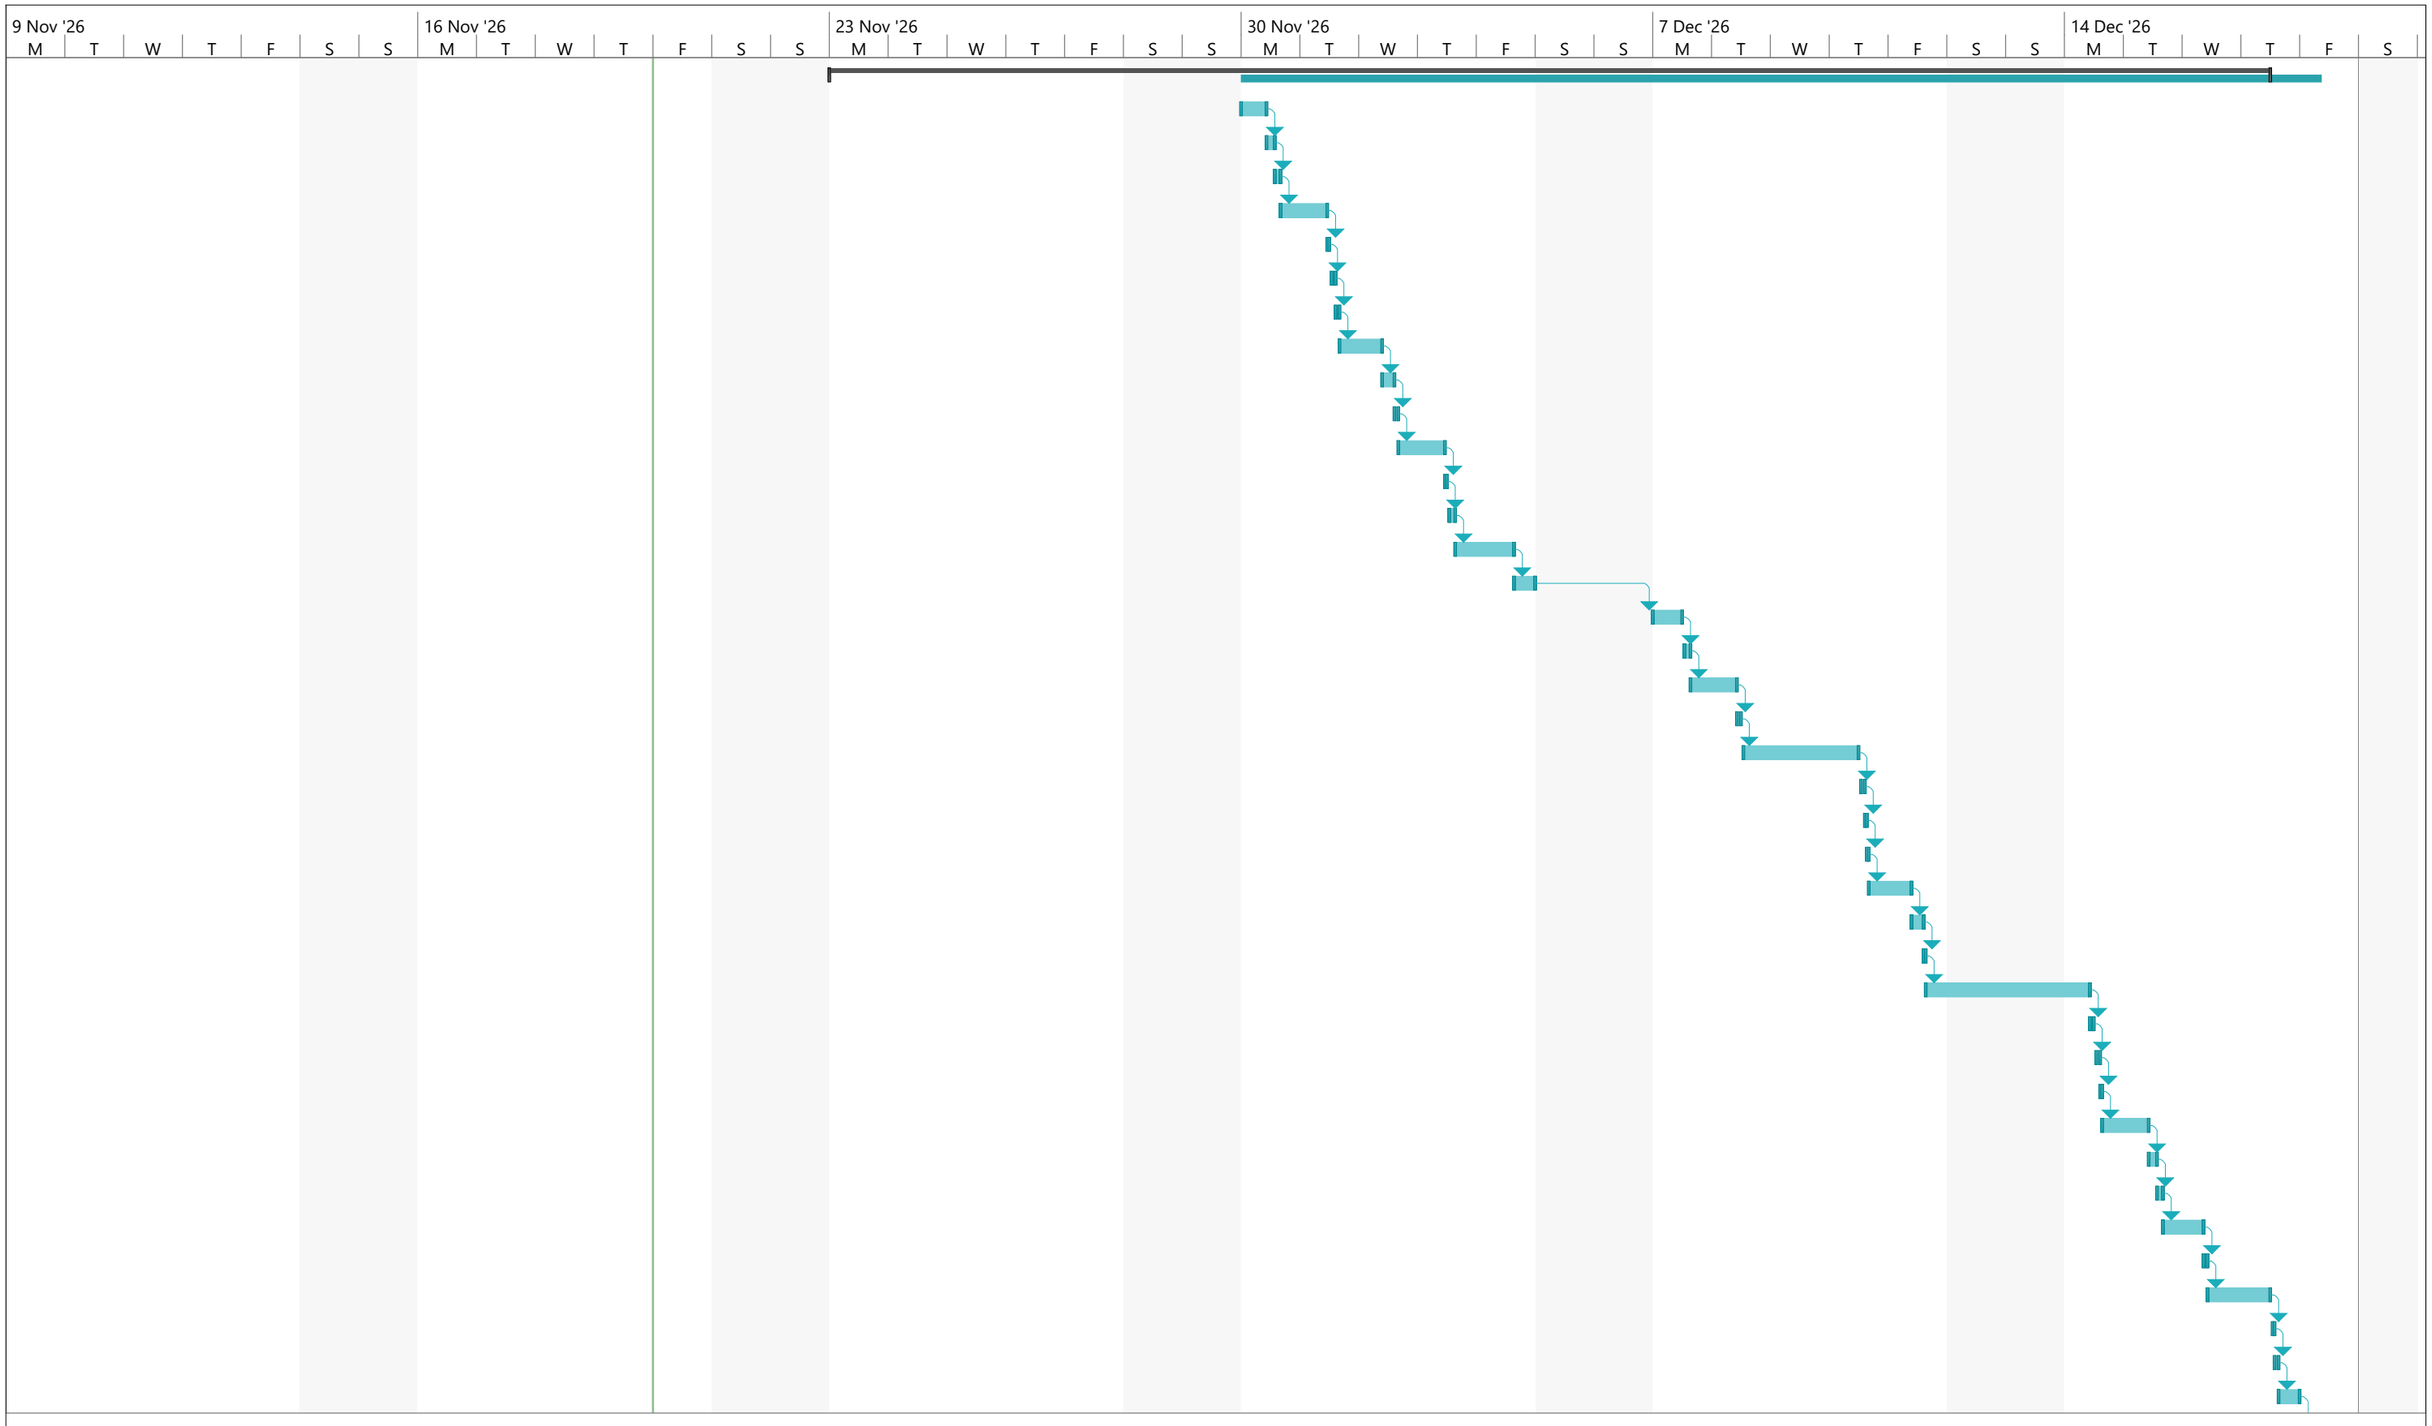

Project: Mackenzie DC 26-27 R
Date: Fri 20/11/26

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	

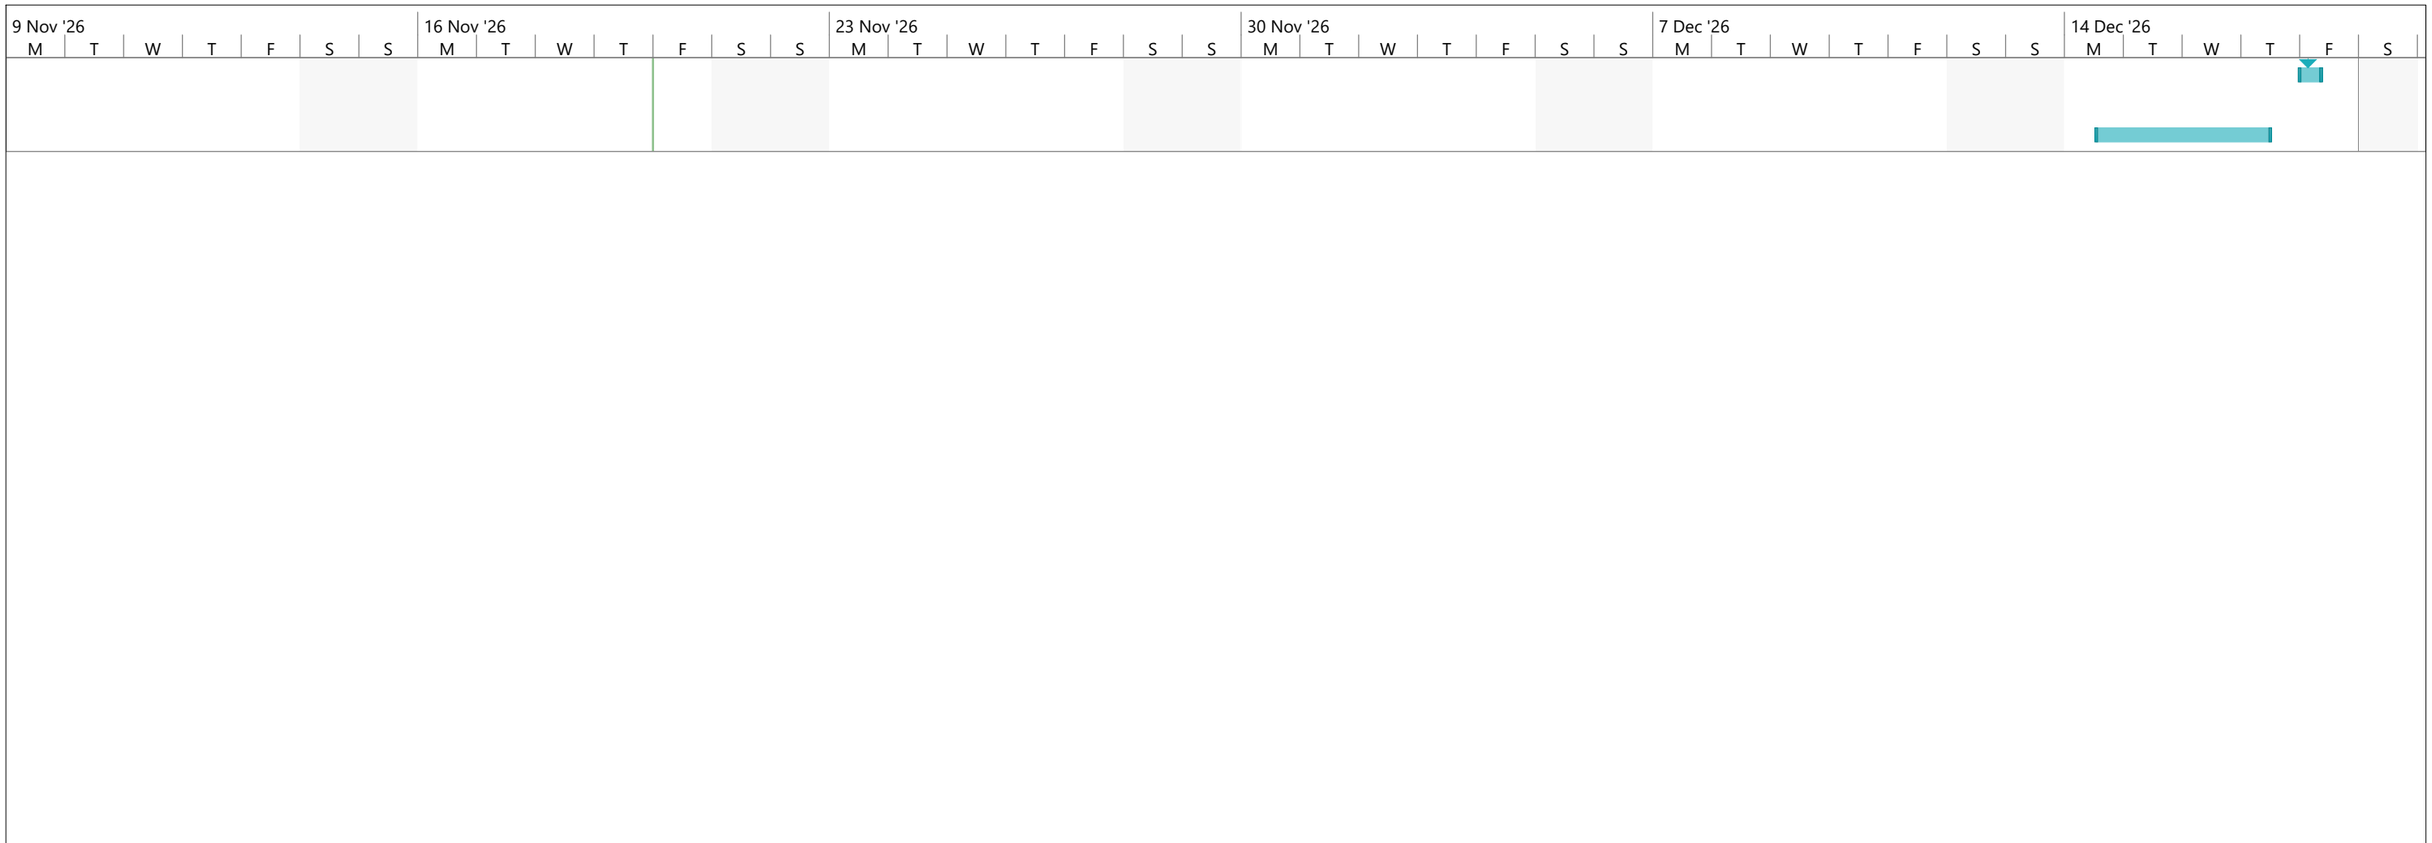

Project: Mackenzie DC 26-27 R
Date: Fri 20/11/26

Task	Project Summary	Manual Task	Start-only	Deadline	
Split	Inactive Task	Duration-only	Finish-only	Progress	
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress	
Summary	Inactive Summary	Manual Summary	External Milestone		
